PROJECT REPORT

NAME: *MR.MUHAMMAD WAQAR* ***ENROLLMENT: 03-298161-027***

NAME: *MR.MUHAMMAD MUSTAFA KHAN* ***ENROLLMENT: 03-298161-038***

SEMESTER: *Spring-2017, MSPM -III* ***PROGRAM: MS (PROJECT MANAGEMENT)***

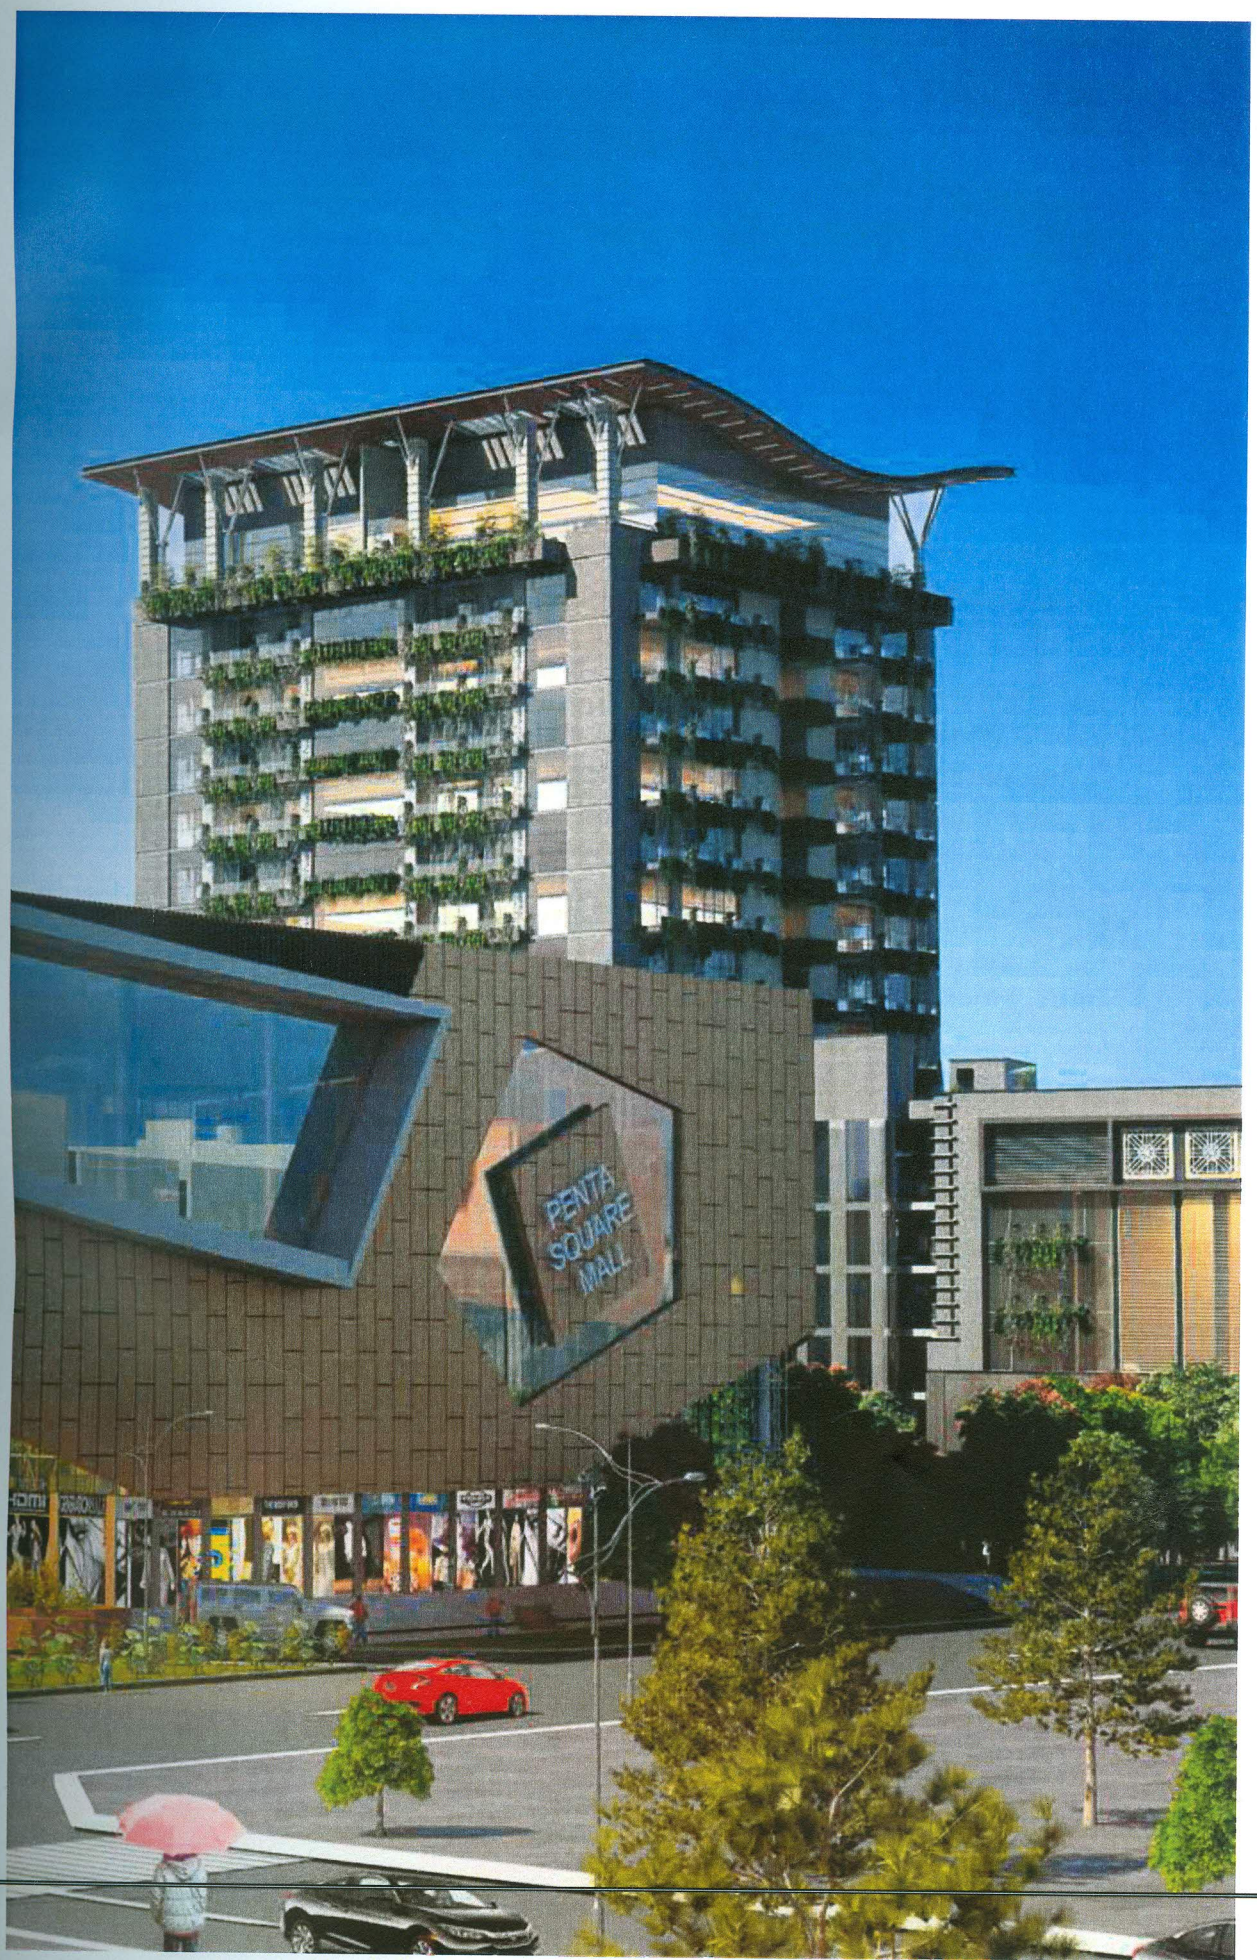
PENTA FIVE SQUARE BY MAAKSON



BAHRIA UNIVERSITY LAHORE CAMPUS

SUBMITTED TO: ***Mr. Muhammad Faisal Shahzad***

SUBMITION DATE: 11-Jun-2017


PENTA
SQUARE
MALL

M.A. Aleem Khan & Sons (Pvt) Ltd.

CERTIFICATE

This witness statement is issued to the applicant for the fulfilment of his/her MS (Project Management) program requirements being carried out at Bahria University Lahore Campus (BULC).

It is witnessed that Mr. Muhammad Waqar Enrollment: 03-298161-027 & Mr. Muhammad Mustafa Khan Enrollment: 03-298161-038 Class: **MSPM-II** Semester: **SPRING 2017** has contacted / visited / frequently utilized our premises /participated in our real-time projects for implementing project management skills using EPM as a leading software tool.

He / She, in case of participation in organization's project, has contributed fully / partially in the following project(s) and within the highlighted fields (planning, scheduling, earned value analysis, performance monitoring, claim debugging):

1. PLANNING

2. SCHEDULING

3. EVM

He / She, in case of visiting/ frequently utilized premises, has been found skillful in applying EPM in the following highlighted fields (planning, scheduling, earned value analysis, performance monitoring, report

M. Wasim Khan
Chief Executive

Table of Contents

LIST OF TABLES iv

LIST OF FIGURE iv

Abstract 2

CHAPTER-1: Introduction 2

1.1: The Company 2

1.1.1 Vision 3

1.1.2 Mission 3

1.1.3 Corporate Strategy 3

1.1.4 Organizational Chart 4

1.2 Project Management 5

1.3 Need for Project Management 5

1.4 Our Project 5

1.5 Project Charter 6

1.5.2 Introduction 8

1.5.7 Project Milestones 8

1.5.8 Stakeholders 9

1.5.10 Project Organization 9

CHAPTER-2: Primavera 10

2.1 About Software 10

2.2 Enterprise Project Structure (EPS) 11

2.3 EPS in Primavera 11

2.4 Organizational Breakdown Structure (OBS) 11

2.5 OBS in Primavera 12

2.6 Work Breakdown Structure (WBS) 12

2.7 WBS in Primavera 13

2.8 Roles in Primavera 13

2.9 Resources in Primavera 14

2.10 Activity Codes in Primavera 14

2.11 Activity Types in Primavera 15

2.11.1 Start & Finish Milestones 15

2.11.2 Resource Dependent 15

2.11.3 Task Dependent 16

2.11.4 Level of Effort *16*

2.11.5 WBS Summary *16*

CHAPTER-3: Primavera Implementation on Project & Primavera Documents *17*

3.1 Project Reports *17*

3.1.1 Project EPS *17*

3.1.4 Project WBS Report *21*

CHAPTER-4: Conclusions & Discussions *22*

Conclusion *22*

ANNEXURE I – LIST OF ABREVIATIONS *22*

ANNEXURE II – CBT Log *23*

ANNEXURE III – Bibliography *24*
