# Mcdonalds Resturant Bahria Town

## FOR GAM Corporation

**NAME:** MR. HASSAN RIAZ

**ENROLLMENT:** 03-298152-039

**SEMESTER:** FALL-2016, MSPM - III


**PROGRAM:** MS (PROJECT MANAGEMENT)




**BAHRIA UNIVERSITY LAHORE CAMPUS**

**SUBMITTED TO:** MR. AHSAN MAQBOOL

**SUBMISSION DATE:** January 15th, 2017

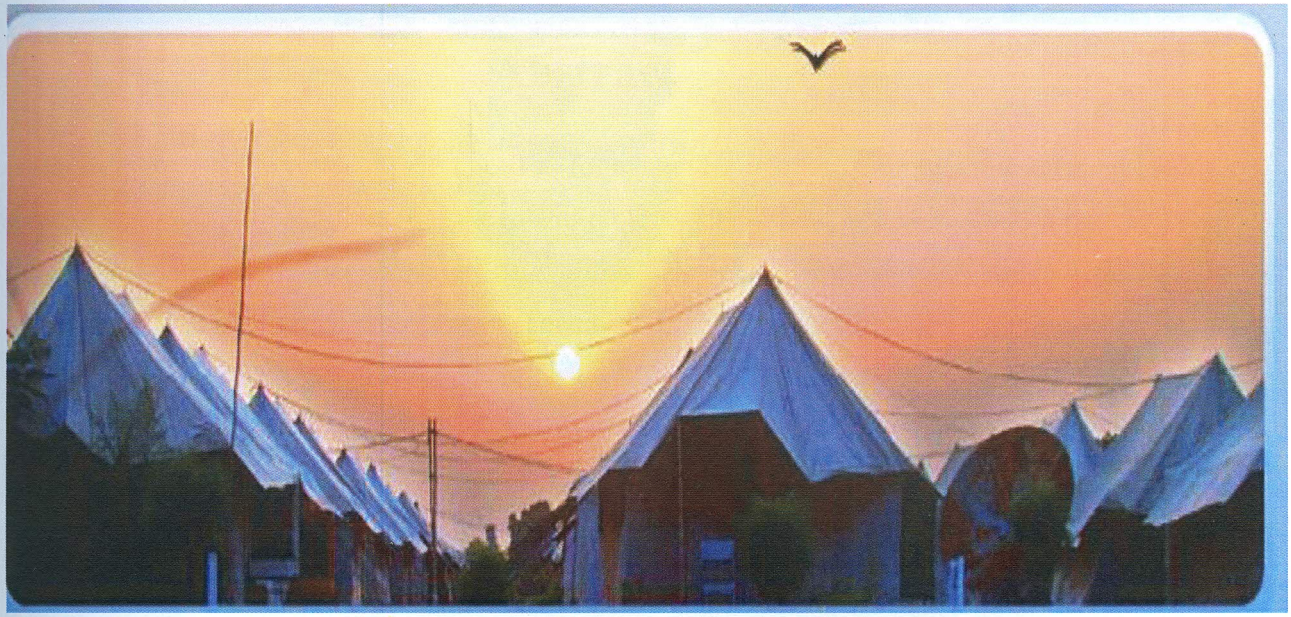

# Acknowledgement

Success and failure is in the hand of Allah. All of above we thanks to Allah Almighty who the creator of knowledge and wisdom for His countless love and help.

The success and final outcome of this project report required a lot of guidance. We sincerely thank to the respected teacher Mr. Ahsan Maqbool for the guidance throughout the project development. I am thankful for their aspiring guidance, invaluably advice during the project work.

Thanks to Parents for their kind support and assistance; otherwise it would have been difficult to keep the constant high spirit of work. The success and final outcome of this project report required a lot of guidance. This project report has indeed helped us to explore more knowledgeable avenues related to the topic and I am sure it will help us in our future.

Regards

Hassan Riaz

MSPM-III, Bahria University Lahore Campus

# Abstract

Many Organizations have identified a need to formalize the practice of project management for developing the coordination center as the role of project management is growing day by day. The Project management office consist of various elements coordination, standardization, optimization and practices of project management

Initially no project plan to fail but according to Standish Group 19% project of total fails and also 46% faces the various challenge. These challenges are delays, budget overruns, or less required features in the end product. These major challenge occur in project because of reactive and uncontrolled delivery, lack of documentation, unrealistic time and budget deadline, short of executive commitment, limited planning. The various addresses and concerns are answered by PMO in this report.

Project Office Management (PMO) for UK Electric has been recommended in this report after detail analyzing the need of PMO within organization. PMO can be defined in several ways but Project Management institute (PMI) can be defined as

"An organizational body or entity assigned various responsibilities related to the centralized and coordinated management of projects under its domain".

Moreover for several selected project in the company the project timeline has been created. We have studied "**Dynamics of PMO and EPM Server**" as an Optional course in the degree program MS (Project Management) at Bahria University Lahore Campus by respected teacher Mr. Ahsan Maqbool who has been kind enough to guide us throughout the course.

## Contents

CERTIFICATE ..... 2

1.1 Introduction ..... 9

1.2 Vision ..... 10

1.3 Mission ..... 10

1.4 Core Values ..... 10

1.4.1 COMMITMENT ..... 10
1.4.2 RESPONSIBILITY ..... 10
1.4.3 COURTESY ..... 10
1.4.4 INTEGRITY ..... 11
1.4.5 COMPETENCE ..... 11
1.5 GEOGRAPHICAL PRESENCE ..... 11
1.6 Organizational Structure ..... 12
1.7 Departments ..... 12
1.8 Projects ..... 13
1.9 Excellence through integrated management system ..... 13
2.1 Introductions to Project Management Office ..... 14
2.1 PMO Framework ..... 14
2.1.1 Process ..... 15
2.1.2 Governance ..... 16
2.1.3 Organization ..... 16
2.1.4 Resources ..... 17
1.2 PMO Roles ..... 18
2.2.1 Supportive ..... 18
2.2.2 Controlling ..... 18
2.2.3 Directive ..... 19
2.3 Types of PMO ..... 19
2.3.1 Weather Station ..... 19
2.3.2 Control Tower ..... 19
2.3.3 Resource Pool ..... 20
2.4 Responsibilities of PMO ..... 20
2.4.1 Establishing Project Methodologies ..... 20
2.4.2 Project Tracking ..... 20

2.4.3 Project Support ..... 21
2.5 Role of Project Managers vs. PMO ..... 21
2.6 Aims and Goals of PMO ..... 22
2.7 Challenges of a PMO ..... 22
2.8 Elements of an Effective PMO ..... 23
3.1 Implementation of PMO in UK Electric ..... 25
3.2 UK Electric Organizational Structure ..... 25
3.4 Major Problems of UK Electric Punjab Region ..... 25
3.5 Project Delivery ..... 26
3.6 Why Need Of PMO ..... 27
PMO at UK Electric Punjab Region ..... 27
3.7 Type of PMO ..... 27
3.8 PMO Implementation ..... 28
3. 8.1 PMO Scope ..... 28
3.8.2 Mission Statement of PMO ..... 28
3.8.3 Vision Statement of PMO ..... 28
Core Values ..... 28
3. 8.4 Stakeholder ..... 29
3.9 Project Management Methodology ..... 29
3.10Project Administrative Support ..... 30
3.11 Training programs ..... 31
3.12 Reporting ..... 31
3.13 Striving for Improvement ..... 31
3.14 Challenges faced in establishing PMO ..... 31
3.14.1 Internal Challenges ..... 31
3.14.2 External Challenges ..... 32
3.14.3 How to tackle these challenges ..... 32

3.15 PMO value addition to UK Electric Punjab Region ..... 32
4 Project ..... 33
4.1 Project Title ..... 33
4.2 Significance with company's business drivers ..... 33
4.3 Project Objectives ..... 34
4.3.1 Success Factors ..... 34
4.4 External Dependencies ..... 34
4.5 Stakeholder Analysis ..... 34
4.6 Project Documents ..... 35
4.7 Implementation Strategy ..... 35
5 Project Charter ..... 36
5.1 Version History ..... 36
5.2 Introduction ..... 36
5.3 Project Objectives ..... 36
5.4 High Level Requirements ..... 36
5.5 Success Criteria ..... 37
5.6 Estimated Timeline ..... 37
5.7 High Level Risks ..... 37
5.8 Constraints & Assumptions ..... 37
5.9 Project Milestones ..... 37
5.10 Stakeholders ..... 38
5.11 Project Budge Estimates ..... 38
5.12 Project Organization ..... 39
5.13 Project Charter Approval ..... 39
6. Project Scope Statement ..... 40
6.1 Version History ..... 41
6.2 Introduction ..... 41

6.3 Project Scope Description ..... 41

6.4 Acceptance Criteria ..... 41

6.5 Project Deliverables ..... 42

6.5 MS Project Sheets ..... 43

Resource Report ..... 45

Network Diagram ..... 47

Resource Sheet ..... 48

Cost Reports ..... 49

In Progress Reports ..... 54

Project Dashboard ..... 55

S Curve ..... 58

References ..... 59

Plagarism Report ..... 60
